

MADI | 19.6

ARCHITECTURE & PLANNING

Measure B Bay View Elementary Campus Updates



APRIL 01, 2020

AGENDA


 MASTER PLAN

 PROJECT BUDGETS

 COMPLETED PROJECTS

 CLASSROOM MODERNIZATION

 FUTURE PLANNING



2018-2019



2019-2020



2020-2021

2020 CAMPUS MASTER PLAN

Bay View Elementary School Bond Projects



Bay View Elementary School – Measure B

PROJECT	START	COMPLETE	PROJECT BUDGET
Multi-Project Overhead	ONGOING	ONGOING	\$689,100
Re-Roofing	COMPLETE	COMPLETE	\$925,529
New Kindergarten Building & Site Work	TBD	TBD	\$0.00
New Classroom Building & Site Work	COMPLETE	COMPLETE	\$3,870,800
Classroom Modernization	04/01/2020	08/7/2020	\$7,400,000
Portable Demolition & Site Work	06/15/2021	08/23/2021	\$550,000
Card Access Security System	06/10/2019	08/21/2021	\$190,000
Data Infrastructure Improvements	06/10/2019	08/21/2021	\$300,000
		TOTAL	\$13,925,429



PROJECT BUDGETS

Bay View Elementary School Bond Projects





PENDANT LIGHTING




ROLLER SHADES



ELECTRONIC LOCKS

CLASSROOM MODERNIZATION:

- NEW BLACKOUT ROLLER SHADES
- NEW LIGHTING
- NEW CEILING & FANS
- NEW CARPET FLOOR
- NEW INTERIOR & EXTERIOR PAINT
- NEW TELEVISIONS
- NEW CLASSROOM FURNITURE
- NEW WINDOW FILM
 - ENERGY EFFICIENCY COATING
 - SECURITY FILM
- NEW ELECTRONIC LOCKS
- HVAC UPGRADES
- ELECTRICAL UPGRADES
- EXTERIOR REPAIRS
- ADA SINKS UPGRADES
- ADA RESTROOM UPGRADES

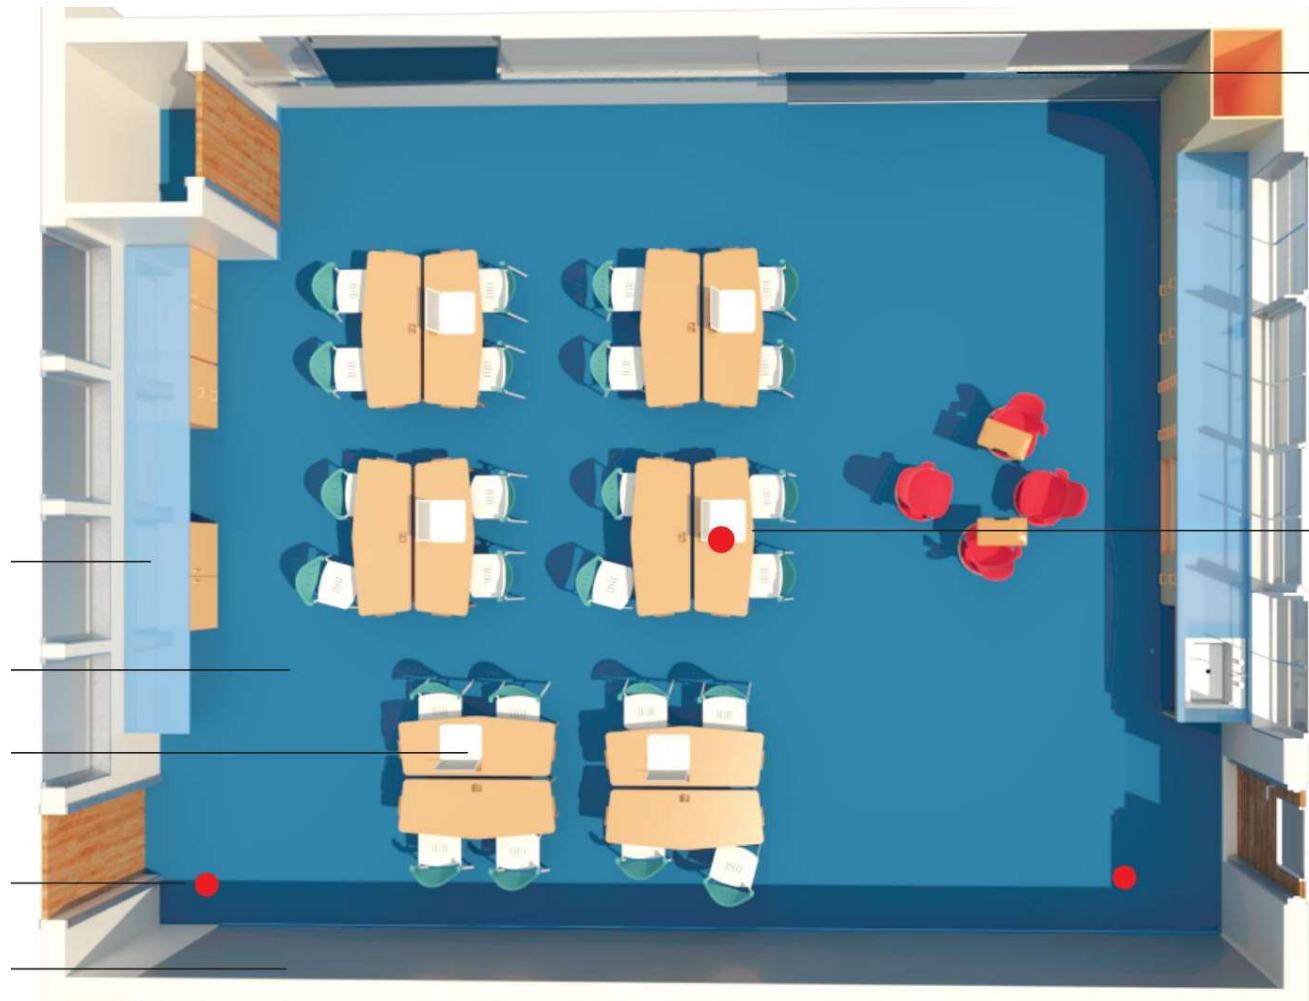

MODERNIZATION – CLASSROOM FINISHES

Bay View Elementary School Bond Projects





MODERNIZATION – CLASSROOM MODERNIZATION RENDER

Bay View Elementary School Bond Projects



KEY DATES:

1. 03/23/2020: START OF CONSTRUCTION
2. 06/08/2020: START OF SUMMER BREAK 2020
3. 08/07/2020: END OF SUMMER BREAK
4. 12/21/2020: START OF WINTER BREAK
5. 12/31/2020: END OF WINTER BREAK

CONSTRUCTION STAGING AREAS:

- 03/23/2020-8/24/2021 (PROJECT DURATION)
- 03/23/2020-08/07/2020



CLASSROOM MODERNIZATION – CONSTRUCTION PHASING

Bay View Elementary School Bond Projects






CAMPUS MODERNIZATION - ADMINISTRATION

Bay View Elementary School Bond Projects




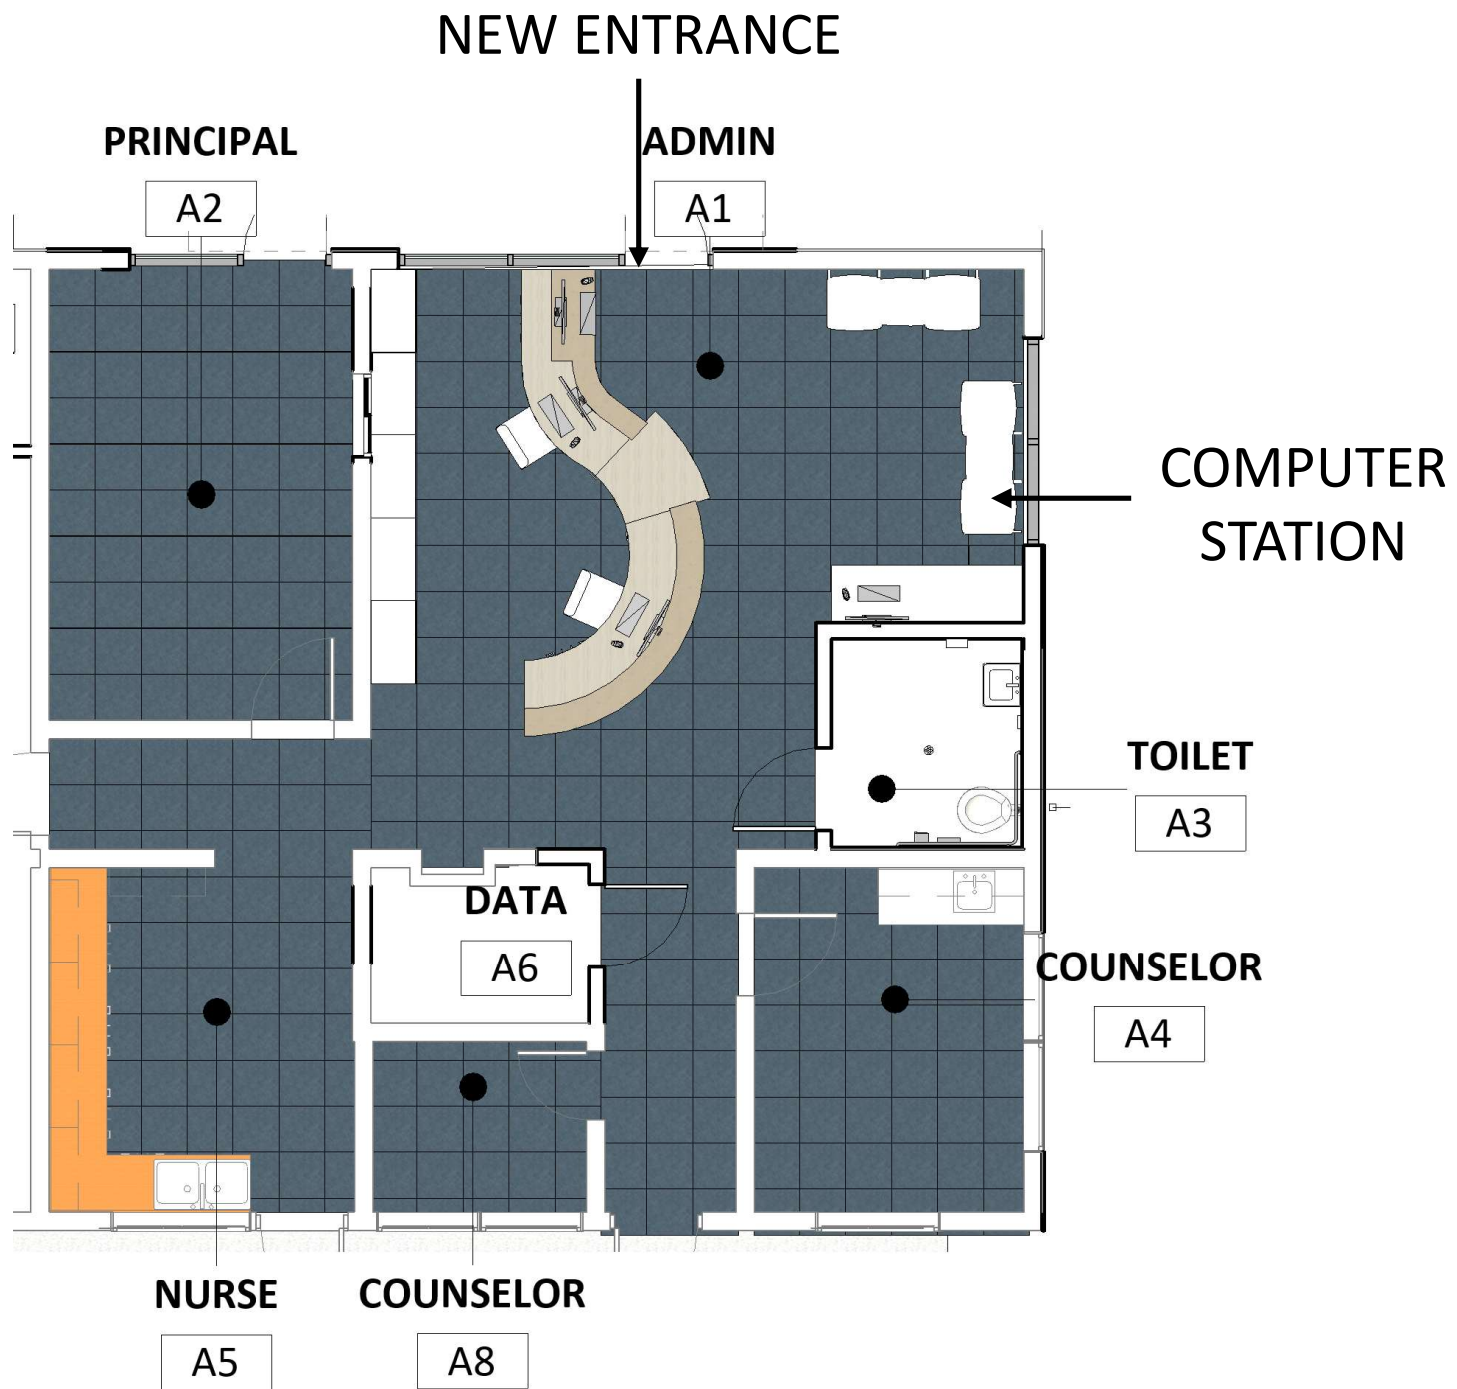

MODERNIZATION – ADMINISTRATION FLOOR PLAN

Bay View Elementary School Bond Projects



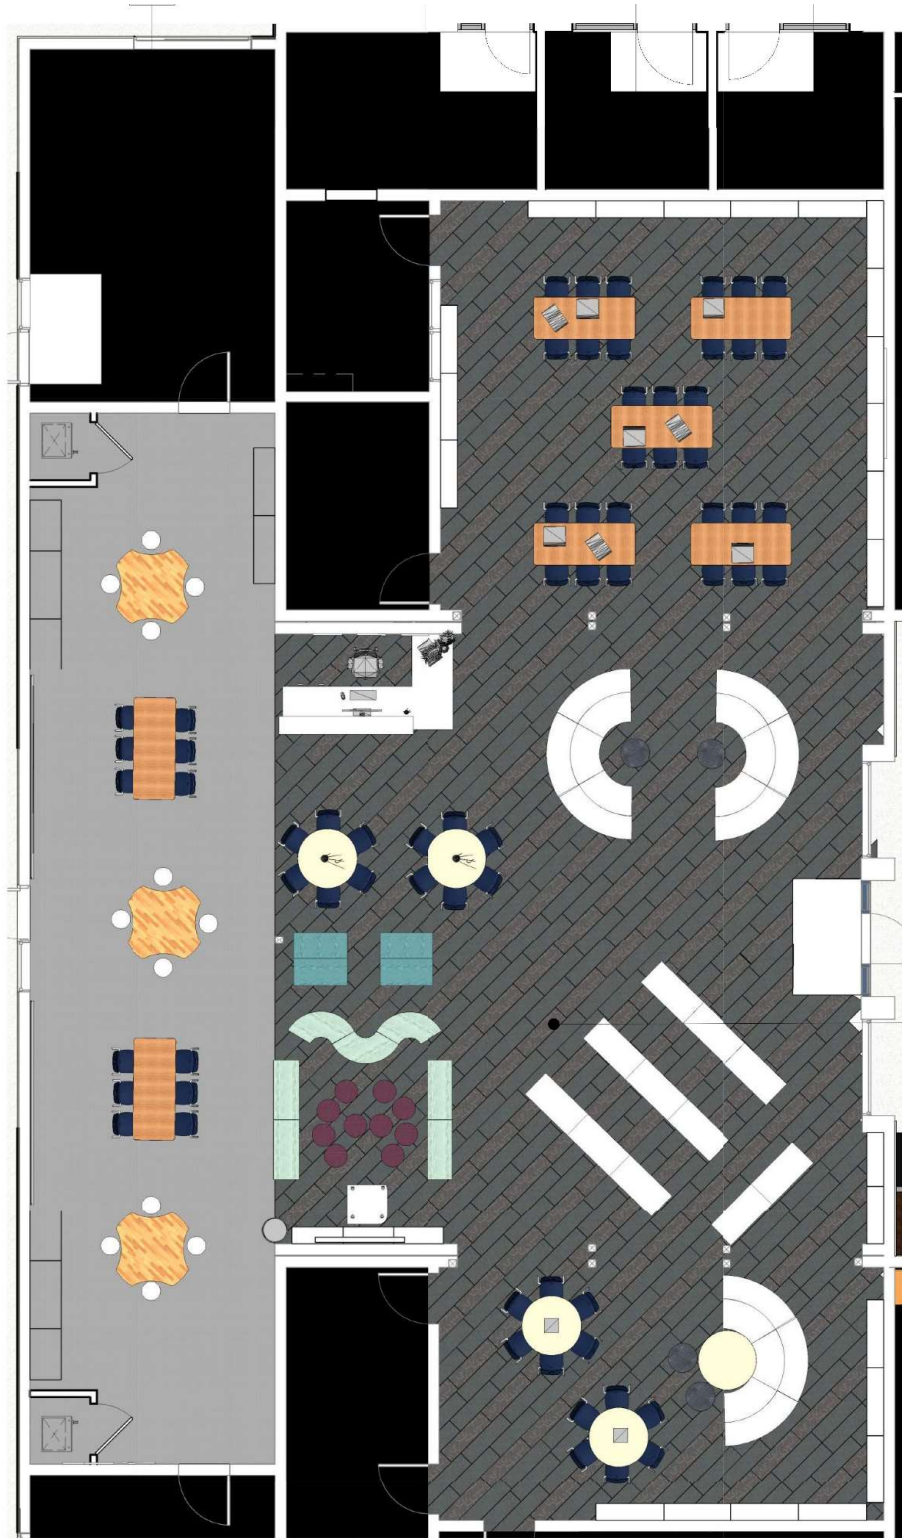

MODERNIZATION – LIBRARY & MEDIA CENTER

Bay View Elementary School Bond Projects





MODERNIZATION – LIBRARY & MEDIA CENTER

Bay View Elementary School Bond Projects





MODERNIZATION – LIBRARY & MEDIA CENTER

Bay View Elementary School Bond Projects





MODERNIZATION – LIBRARY & MEDIA CENTER

Bay View Elementary School Bond Projects





MODERNIZATION – LIBRARY & MEDIA CENTER

Bay View Elementary School Bond Projects



PLAYGROUND STRIPING TO BE DETERMINED WITH STAFF



PHASE 1



PHASE 2

LEGEND

- 01 BASKETBALL COURT
- 02 TETHERBALL COURTS
- 03 BALL WALL
- 04 HANDBALL
- 05 FOURSQUARE COURTS
- 06 COLOR CIRCLE
- 07 NINE SQUARE COURT
- 08 RUNNING & RELAYS
- 09 SHADE STRUCTURE
- 10 TREE
- 11 PORTABLE
- 12 USA MAP (OPTIONAL)
- 13 PLAYGROUND

ASPHALT
BLACKTOP



CAMPUS MODERNIZATION – FUTURE PLAYGROUND

Bay View Elementary School Bond Projects



NEXT PROJECTS:

▲ CLASSROOM MODERNIZATION

- CONSTRUCTION EST. MARCH 2020-AUGUST 2020

▲ FUTURE PROJECTS

- PORTABLE DEMOLITION/PLAYGROUND EXPANSION

▲ UNFUNDED PROJECTS (FUTURE BOND)

- PLANNING FOR FUTURE KINDERGARTEN CLASSROOMS
- SPECIAL NEEDS CLASSROOMS



WHAT'S NEXT

Bay View Elementary School Bond Projects



THANK YOU!
